

Project Title	Seagreen Wind Energy Ltd
Document Reference Number	LF000009-MIP-MA-MAN-NOT-0001

Seagreen Offshore Wind Farm.

Weekly Notice of Operations 43/2023

Issue Date – 23rd of October 2023.

Notice of Operations on Seagreen Offshore Wind Farm.

Work planned for the period 23-10-2023 to 29-10-2023.

Construction activities commenced on Seagreen Offshore Wind Farm on Thursday 17th December 2021.

This notice will be updated weekly giving information of the progress and resources involved in the construction of the windfarm. The intention is to give notice of the activities involved in the construction phase of the project. Should anyone have any questions regarding construction operations we kindly ask that you put them forward well in advance.

The Seagreen Offshore Wind Farm is located in the outer Firth of Forth and Firth of Tay region of the North Sea. The site is situated approximately 17.5 nautical miles East-southeast of the Port of Montrose where the project Marine Coordination Centre will be located during the construction and operational phases. The first phase of the development will consist of 114 suction bucket foundation structures, with associated 114 10MW offshore wind turbine generators, 1 HVAC offshore substation platform, associated inter array and export cabling. The generated power will be transmitted to the National Grid via 3 subsea transmission cables making landfall at Carnoustie, Angus, to the Southwest of the development site. Grid connection will be achieved at the Tealing onshore substation. The second phase of the project will consist of 36 piled foundation structures, with associated 36 Wind Turbine Generators, associated inter array and export cabling and one additional 1 HVAC offshore substation platform. The phase 2 transmission cable is proposed to make landfall at Cockenzie, East Lothian (subject to appropriate licensing).

The Seagreen development site is highlighted below in red, the export cable corridor is highlighted in blue.

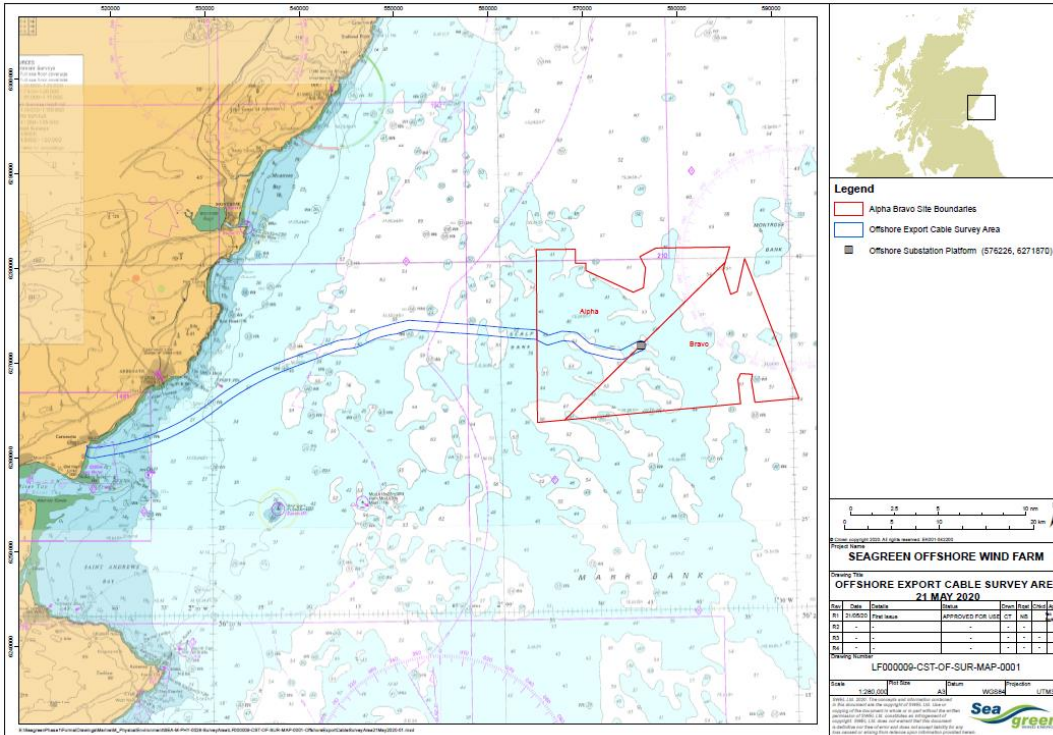


Fig 1 – Seagreen offshore wind farm location and export cable corridor.

1. Contact details for Marine Coordination


The following contact can provide more information if required.

Telephone Number (24/7 Operations)	+44 (0) 1674 689401
Email for Marine Coordinator	seagreenmarinecoordination@sse.com
Address	Seagreen Wind Energy Ltd, O&M Building, Windy Waves House, South Quay Ferryden, Montrose, Angus DD10 9SL

2. Wind Turbine Generator Installation & Commissioning.


On behalf of Seagreen Wind Energy Ltd, MHI Vestas Offshore Wind continue wind turbine generators works.


The Service Operation Vessel (SOV) Norside Cetus will provide accommodation for WTG commissioning technicians. Personnel will utilise a walk to work gangway systems to access the WTG structures for work activities.

Vessel – Norside Cetus	Contact Details	
	Call Sign	LNCQ3
	MMSI	257931000
	Length	83.4m
	Beam	18.0m
	Draft	5.6m
	Vessel Contact	Paul Grant – Commissioning Manager +44 7587630374

3. Crew Transfer Vessels (CTV's).

A number of crew transfer vessels support operations within the Seagreen site, please see details below.

Vessel – GXS Valtos	Contact Details	
	Call Sign	2FDO4
	MMSI	235090347
	Length	22m
	Beam	6m
	Draft	1.8m
	Vessel Contact	Euan Mowatt – Seaway 7 07539 368974


Vessel – Windcat 101	Contact Details	
	Call Sign	2ELU3
	MMSI	235086213
	Length	27.86m
	Beam	9.32m
	Draft	1.9m
	Vessel Contact	Graeme.watters@sse.com

4. Construction progress update.

Installation and Commissioning of the Seagreen Offshore Sub-station platform, export cable, inter-array cables and 114 wind turbine generators is now complete. Installation coordinates of the WTG’s can be obtained by via the Duty Marine Coordinator, contact details in section 1.


5. Guard Vessel Deployment.


Seagreen Wind Energy have deployed a site Guard Vessel. Six hourly VHF radio broadcasts shall be made containing information regarding the Seagreen development including installation activity, safety zone information and site demarcation buoyage information. Vessel details below.

Vessel – Evening Star	Contact Details	
	Call Sign	MNEP3
	MMSI	235006716
	Length	21m
	Beam	6m
	Draft	5m

6. Operations & Maintenance

Operations & Maintenance activities are underway with all the wind turbine generators fully commissioned. Technicians shall be deployed to service the WTG's and carry out any required troubleshooting tasks. The Operations & Maintenance team shall be deployed from the service operations vessel Edda Brint and crew transfer vessel MO6.

Vessel – Edda Brint		Contact Details		
	Call Sign	LALG8		
	MMSI	257967000		
	Length	82.0m		
	Beam	19.0m		
	Draft	5.0m		
	Vessel Contact	Graeme.watters@sse.com		

Vessel – MO6		Contact Details		
	Call Sign	MIQO2		
	MMSI	232033197		
	Length	26.0m		
	Beam	11.0m		
	Draft	2.7m		
	Vessel Contact	Graeme.watters@sse.com		

7. Offshore Fisheries Liaison Officers.

During the construction phase of the Seagreen project there will be Offshore Fisheries Liaison Officers (OFLO) deployed on selected construction vessels. The principal role of the OFLO is to establish and maintain effective communications with any fishing vessels encountered and to monitor compliance with good practice guidelines whilst doing so. The OFLO will record details of any fishing activity in and around the site including fishing vessels, gear and communications with fishing vessels and will provide regular updates to the Seagreen FLO. Please contact Seagreen Marine Coordination for further information.

8. Safety Zones.

Following consideration by Scottish government ministers it has been agreed that during the construction phases of the Seagreen development mandatory rolling 500m safety zones will be established around each Wind Turbine Generator and/or their foundations whilst construction works are in progress, as indicated by the presence of a construction vessel. The safety zones will be triggered whenever a vessel is on station at a WTG and undertaking construction activities.

In addition, mandatory pre commissioning 50m safety zones will be established around each Wind Turbine Generator and/or their foundations when construction works have been completed but prior to Wind Farm commissioning or where construction works have only been partially completed. These safety zones will be active at any structure during the construction phase where a construction vessel is not present at a Wind Turbine Generator.

9. Website

The official website for Seagreen Offshore Wind Farm can be found at

<https://seagreenwindenergy.com>

This contains all Seagreen Weekly Notices of Operations and Notices to Mariners, together with a large amount of general information about the project.







There is also a Twitter feed at [@seagreenwind](#)

10. Distribution List

A central list of recipients is maintained by Seagreen Marine Coordination, if you are not the appropriate recipient or do not wish to receive these notices, please contact Marine Coordination as per the details in section 1 of this notice.

This document contains proprietary information belonging to Seagreen Wind Energy Ltd or affiliated companies and shall be used only for the purpose for which it was supplied. It shall not be copied, reproduced, disclosed or otherwise used, nor shall such information be furnished in whole or in part to third parties, except in accordance with the terms of any agreement under which it was supplied or with the prior consent of Seagreen Wind Energy Ltd and shall be returned upon request. © Copyright of Seagreen Wind Energy Ltd.

11. Seagreen weekly vessel report.

Seagreen Offshore Windfarm Vessels & Operators										23.10.2023
Reference to Marine Licence Conditions 3.1.2 (OWF Alpha and Bravo ML), 3.1.2 (OTA ML) and 3.1.2 (Open Cut at Landfall ML)										
Vessel Data Matrix OWF/OTA/Open Cut at Landfall										
#	Vessel Picture	Vessel Name / Flag	Type / Function	Operator	Contact / contact details	Call sign / MMSI / IMO	LOA (m) Beam (m) D (m)	Date on Site	Marine Licence(s) applicable	
1		Edda Brint	Service Operations Vessel	Vestas	Graeme Watters Lead Marine Coordinator +44 (0) 7932 229828	LALG8 257967000	82.85m x 18.60m	14/05/2023	OWF Alpha & Bravo ML	
2		MO6	Crew Transfer vessel	SWEL	Graeme Watters Lead Marine Coordinator +44 (0) 7932 229828	MIQO2 232033197	26m x 11m	04.07.23	OWF Alpha & Bravo ML	
3		GKS Valtos	Crew Transfer vessel	Seaway7	Euan Mowatt Seaway 7 +44 (0) 7539368974	2FDO4 235090347	22.0m x 6.0m	19.03.23	OWF Alpha & Bravo ML	
4		Norside Cetus	Multi Purpose Offshore Vessel	Vestas	Paul Grant Vestas +44 7587630374	LNCQ3 257931000	83.4m x 18.0m	22.01.23	OWF Alpha & Bravo ML	
5		Windcat 101	Crew Transfer vessel	Petrofac	Graeme Watters Lead Marine Coordinator +44 (0) 7932 229828	2ELU3 235086213	28.0m x 9.0m	24.08.23	OTA ML	
6		GV Evening Star	Guard Vessel	Seagreen Wind Energy Ltd.	Graeme Watters Lead Marine Coordinator +44 (0) 7932 229828	MNEP3 235006716	21.0m x 7.0m	16.10.23	OWF Alpha & Bravo ML	
