

Project Title	Seagreen Wind Energy Ltd
Document Reference Number	LF000009-MIP-MA-MAN-NOT-0001

Seagreen Offshore Wind Farm

Weekly Notice of Operations

37/2025

Issue Date – 8th September 2025.

Notice of Operations on Seagreen Offshore Wind Farm.

Work planned for the period 08-09-25 to 14-09-25.

Construction activities commenced on Seagreen Offshore Wind Farm on Thursday 17th December 2021. The first phase of the project is now fully operational with all 114 Wind Turbine Generators fully commissioned. As such, Operations and Maintenance activities are underway. There are several outstanding construction activities remaining which will be ongoing during 2025. This notice will be updated weekly giving information on all the activities taking place in the windfarm. Should anyone have any questions regarding construction operations we kindly ask that you put them forward well in advance.

The Seagreen Offshore Wind Farm is located at the outer Firth of Forth and Firth of Tay region of the North Sea. The site is situated approximately 17.5 nautical miles East-southeast of the Port of Montrose where the project Marine Coordination Centre is located. The development consists of 114 suction bucket foundation structures, with associated 10MW wind turbine generators, 1 HVAC offshore substation platform, associated inter array and export cabling. The generated power is transmitted to the National Grid via three subsea transmission cables making landfall at Carnoustie, Angus. Grid connection has been achieved at the Tealing onshore substation.

The Seagreen development site is highlighted below in red, the export cable corridor is highlighted in blue.

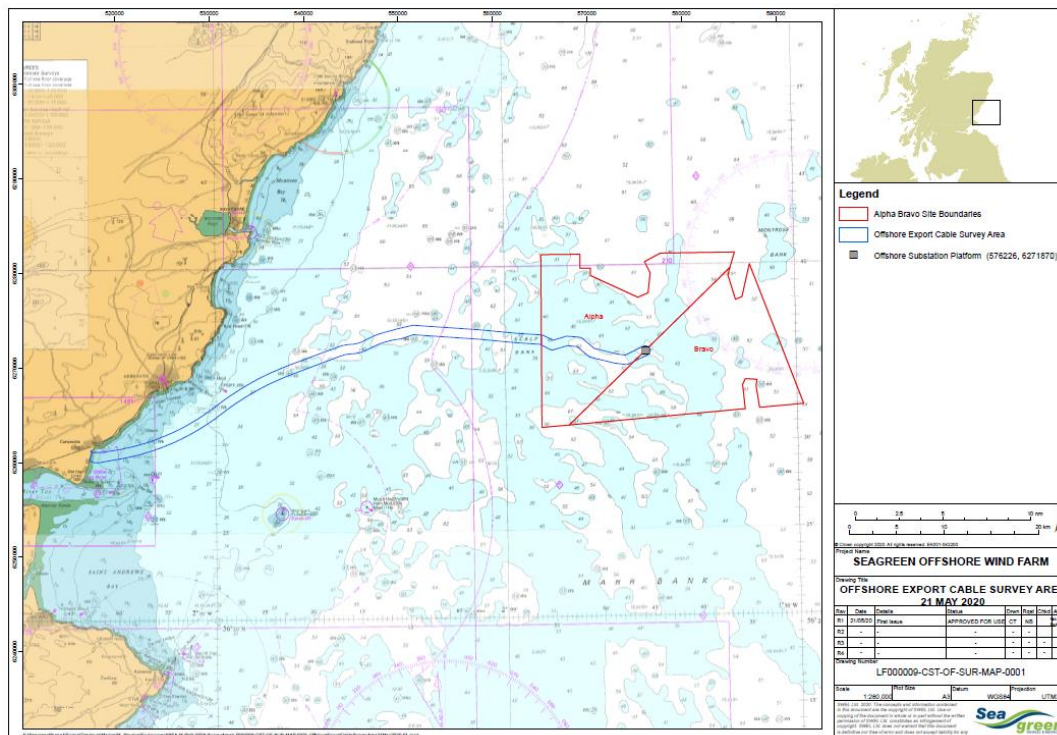


Fig 1 – Seagreen offshore wind farm location and export cable corridor.

1. Contact details for Marine Coordination

The following contact can provide more information if required.

Telephone Number (24/7 Operations)	+44 (0) 1674 689401
Email for Marine Coordinator	seagreenmarinecoordination@sse.com
Address	Seagreen Wind Energy Ltd, O&M Building, Windy Waves House, South Quay Ferryden, Montrose, Angus DD10 9SL

2. Operations & Maintenance activities (O&M)

Operations and Maintenance activities are ongoing. The Service Operation Vessel (SOV) Brint Enabler will provide accommodation with personnel utilising a walk to work gangway system to access the WTG structures for work activities. Operations are 24 hours per day. The CTV, MO9, will support the Brint Enabler with O&M operations.

Vessel – Brint Enabler.	Contact Details	
	Call Sign	LALG8
	MMSI	257967000
	Length	82.0m
	Beam	18.5m
	Draft	4.9m

Vessel – MO9	Contact Details	
	Call Sign	MNXA2
	MMSI	232048583
	Length	26.0m
	Beam	11.0m
	Draft	2.7m

3. Offshore Substation Platform Works

SSE will commence a short programme of works at the Seagreen Offshore Sub-station platform. The CTV Farra Grainne will be supporting operations with Island Diligence.

Vessel – Island Diligence	Contact Details	
	Call Sign	LAVG7
	MMSI	258687000
	Length	86.0m
	Beam	18.5m
	Draft	5.5m

Vessel – Farra Grainne	Contact Details	
	Call Sign	MNOZ3
	MMSI	232047463
	Length	27m
	Beam	9m
	Draft	1.7m

4. Guard Vessel Deployment.

Seagreen Wind Energy have deployed a site Guard Vessel. Six hourly VHF radio broadcasts shall be made containing information regarding the Seagreen development including work activities, safety zone information and site demarcation buoyage information. Vessel details below. GV Courage SH170 to relieve GV Ocean Quest DTG tbc.

Vessel – GV Courage SH170	Contact Details	
	Callsign	MDJL4
	MMSI	233308000
	Length	26m
	Beam	7.5m
	Draft	4.25m
Vessel – GV Ocean Quest	Contact Details	
	Callsign	MSBS6
	MMSI	232004618
	Length	21m
	Beam	7m
	Draft	3m

5. Safety Zones

As all the Seagreen Wind Turbine Generators are fully commissioned, mandatory 500m safety zones shall be established around any WTG where major maintenance work is being undertaken, where major maintenance is as per the definition given in the 2007 Regulations. The safety zones will be active whenever a major maintenance vessel is at the WTG during the operational phase. Up to five of these safety zones could be concurrently active, but no more than four where there is one active 500m safety zone around the Offshore Sub-station Platform.

A mandatory 500m safety zone shall be established around the Offshore Sub-station Platform where major maintenance work is being undertaken, where major maintenance is as per the definition given in the 2007 Regulations. The safety zone will be active whenever a major maintenance vessel is at the OSP during the operational phase.

6. Website

The official website for Seagreen Offshore Wind Farm can be found at

<https://seagreenwindenergy.com>

This contains all Seagreen Weekly Notices of Operations and Notices to Mariners, together with a large amount of general information about the project.

There is also a Twitter feed at [@seagreenwind](#)

7. Distribution List

A central list of recipients is maintained by Seagreen Marine Coordination, if you are not the appropriate recipient or do not wish to receive these notices, please contact Marine Coordination as per the details in section 1 of this notice.

This document contains proprietary information belonging to Seagreen Wind Energy Ltd or affiliated companies and shall be used only for the purpose for which it was supplied. It shall not be copied, reproduced, disclosed or otherwise used, nor shall such information be furnished in whole or in part to third parties, except in accordance with the terms of any agreement under which it was supplied or with the prior consent of Seagreen Wind Energy Ltd and shall be returned upon request. © Copyright of Seagreen Wind Energy Ltd.

8. Seagreen weekly vessel report.

Seagreen Offshore Windfarm Vessels & Operators									
Reference to Marine Licence Conditions 3.1.2 (OWF Alpha and Bravo ML), 3.1.2 (OTA ML) and 3.1.2 (Open Cut at Landfall ML)									
Vessel Data Matrix Seagreen Windfarm									
No	Vessel Picture	Vessel Name / Flag	Type / Function	Operator	Contact / contact details	Call sign / MMSI / IMO	LOA (m) Beam (m) Draft	Date on Site	Marine Licence(s) applicable
1		Brint Enabler	Service Operations Vessel	Vestas	Seagreen Marine Coordination +44 (0) 1674 689401	LALG8 257967000	82m x 18m	04.04.24	N/A
2		MO9	Crew Transfer Vessel	Vestas	Seagreen Marine Coordination +44 (0) 1674 689401	MNXA2 232048583	26m x 11m	02.12.23	N/A
3		Island Diligence	Service Operations Vessel	SWEL	Seagreen Marine Coordination +44 (0) 1674 689401	LAVG7 258687000	86m x 18.5	15.08.2025	N/A
4		Farra Grainne	Crew Transfer Vessel	SWEL	Seagreen Marine Coordination +44 (0) 1674 689401	MNOZ3 232047463	27m x 9m	25.07.2025	N/A
5		GV Ocean Quest	Guard Vessel	SWEL	Seagreen Marine Coordination +44 (0) 1674 689401	MSBS6 232004618	21m x 6m	28.08.2025	N/A
5		GV Courage SH170	Guard Vessel	SWEL	Seagreen Marine Coordination +44 (0) 1674 689401	MDIL4 233308000	26m x 7m	TBC	N/A
