

Project Title	Seagreen Wind Energy Ltd
Document Reference Number	LF000009-MIP-MA-MAN-NOT-0001

Seagreen Offshore Windfarm Ltd.

Weekly Notice of Operations 12/2021

Issue Date – 22nd March 2021.

Notice of Operations on Seagreen Offshore Windfarm.

Work planned for the period 22-03-2021 to 28-03-2021.

Construction activities commenced on Seagreen Offshore Windfarm on Thursday 17th December with works at the export cable landfall site. This notice will be updated weekly giving information of the progress and resources involved in the construction of the windfarm. The intention is to give notice of the activities involved in the construction phase of the project. Should anyone have any questions regarding construction operations we kindly ask that you put them forward well in advance.

The Seagreen Offshore Windfarm is located in the outer Firth of Forth and Firth of Tay region of the North Sea. The site is situated approximately 17.5 nautical miles East-southeast of the Port of Montrose where the project Marine Coordination Centre will be located during the construction and operational phases. The first phase of the development will consist of 114 suction bucket foundation structures, with associated 114 10MW offshore wind turbine generators, 1 HVAC offshore substation platform, associated inter array and export cabling. The generated power will be transmitted to the National Grid via 3 subsea transmission cables making landfall at Carnoustie, Angus, to the Southwest of the development site. Grid connection will

be achieved at the Tealing onshore substation. The second phase of the project will consist of 36 piled foundation structures, with associated 36 Wind Turbine Generators, associated inter array and export cabling and one additional 1 HVAC offshore substation platform. The phase 2 transmission cable is proposed to make landfall at Cockenzie, East Lothian (subject to appropriate licensing).

The Seagreen development site is highlighted below in red, the export cable corridor is highlighted in yellow.

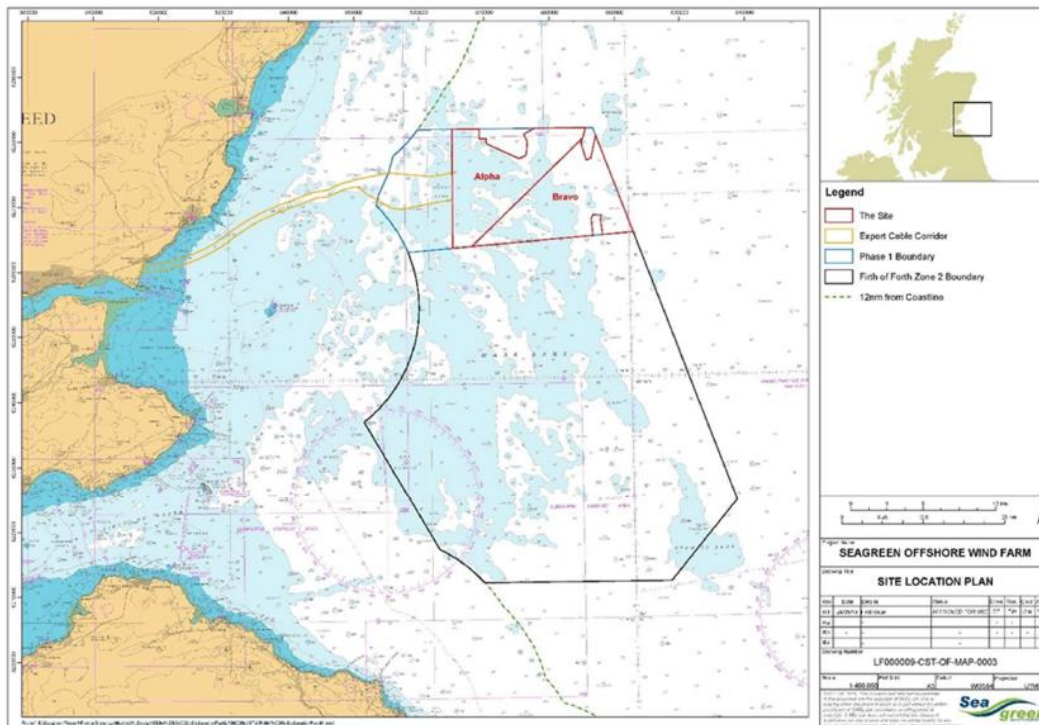


Fig 1 – Seagreen offshore windfarm location and export cable corridor.

1. Contact details for Marine Coordination

The following contact can provide more information if required.

Telephone Number (Day Operations)	+44 (0) 7932 229828
Email for Marine Coordinator	seagreenmarinecoordination@sse.com
Address	Seagreen Wind Energy Ltd, 1 Waterloo Street Glasgow, G2 6AY

2. Ongoing Operations

2.1 Export Cable Landfall works.

Works continue at the export cable landfall site, with completion of the outer sheet piled cofferdam last week. Commencement of the inner cofferdam commences this week and this will involve construction of a temporary piling platform. Once the cofferdam is in place this will then allow the excavation and installation of cable ducts, cement bound sand and final backfill. The landfall works area is shown below in Fig 2.



Fig 2 – Landfall works area located at Carnoustie Barry Golf Links.

3. Unexploded Ordnance & Boulder clearance Geophysical Survey works.

An unexploded ordnance and boulder clearance geophysical survey will take place within the Seagreen Offshore Windfarm site boundary. The survey vessel, Geo Ranger will utilise towed array equipment with side scan sonar, sub bottom profiler and magnetometer to conduct the survey of all 114 Wind Turbine Generator positions and 1 Offshore Platform location within the Seagreen site boundary.

The survey vessel arrived at site on Saturday the 20th of March. Survey works are expected to be concluded by August 21 however this period may be extended due to weather conditions.

The coordinates of the Seagreen site boundary are below in Table 1 and shown in Fig 1. Details of the survey vessel, Geo Ranger are shown in Table 2.

ID	Latitude (DDM WGS 84)	Longitude (DDM WGS 84)
01	56° 40.631' N	1° 43.829' W
02	56° 40.606' N	1° 36.151' W
03	56° 39.317' N	1° 36.884' W
04	56° 37.913' N	1° 36.151' W
05	56° 39.923' N	1° 34.627' W
06	56° 31.903' N	1° 29.311' W
07	56° 31.724' N	1° 33.882' W
08	56° 32.983' N	1° 34.195' W
09	56° 33.051' N	1° 35.583' W
10	56° 31.666' N	1° 35.352' W
11	56° 30.803' N	1° 56.378' W
12	56° 40.653' N	1° 56.226' W
13	56° 40.648' N	1° 52.170' W
14	56° 39.836' N	1° 51.101' W
15	56° 38.138' N	1° 46.249' W
16	56° 38.383' N	1° 45.181' W
17	56° 40.157' N	1° 45.487' W

Table 1 – Site Boundary coordinates.

Vessel Name – Geo Ranger	
General Description and Dimensions:	Survey vessel. 41.2m LOA, 8.7m beam, 2.4m draught
Call Sign:	PHHV
MMSI:	245893000
Satellite communications details	00 870 776 257 317
Direct Bridge/ Masters Number	+31 316 728 130
Onshore Representative:	Alexandru Lepadatu, Alexandru.Lepadatu@subsea7.com

	+31(0)61 057 48 75
Onboard Survey rep.	Gary Howes, +44 (0)7919 155748
Offshore Fisheries Liaison Officer	Peter Gatt, +44 (0) 7880 936272



Table 2 – Survey Vessel Geo Ranger.

4. Distribution List

A central list of recipients is maintained by Seagreen Marine Coordination, if you are not the appropriate recipient or do not wish to receive these notices please contact Marine Coordination as per the details in section 1 of this notice.

5. Website

The official website for Seagreen Offshore Windfarm can be found at

<https://seagreenwindenergy.com>

This contains all Seagreen Weekly Notices of Operations and Notices to Mariners, together with a large amount of general information about the project.

There is also a Twitter feed at [@seagreenwind](https://twitter.com/seagreenwind)



Document Reference

LF000009-MIP-MA-MAN-NOT-0001

Rev: 15

Page 6 of 6

This document contains proprietary information belonging to Seagreen Wind Energy Ltd or affiliated companies and shall be used only for the purpose for which it was supplied. It shall not be copied, reproduced, disclosed or otherwise used, nor shall such information be furnished in whole or in part to third parties, except in accordance with the terms of any agreement under which it was supplied or with the prior consent of Seagreen Wind Energy Ltd and shall be returned upon request. © Copyright of Seagreen Wind Energy Ltd
