

Project Title	Seagreen Wind Energy Ltd
Document Reference Number	LF000009-MIP-MA-MAN-NOT-0001

Seagreen Offshore Wind Farm.

Weekly Notice of Operations 28/2021

Issue Date – 12th July 2021.

Notice of Operations on Seagreen Offshore Wind Farm.

Work planned for the period 12-07-2021 to 18-07-2021.

Construction activities commenced on Seagreen Offshore Wind Farm on Thursday 17th December with works at the export cable landfall site. This notice will be updated weekly giving information of the progress and resources involved in the construction of the windfarm. The intention is to give notice of the activities involved in the construction phase of the project. Should anyone have any questions regarding construction operations we kindly ask that you put them forward well in advance.

The Seagreen Offshore Wind Farm is located in the outer Firth of Forth and Firth of Tay region of the North Sea. The site is situated approximately 17.5 nautical miles East-southeast of the Port of Montrose where the project Marine Coordination Centre will be located during the construction and operational phases. The first phase of the development will consist of 114 suction bucket foundation structures, with associated 114 10MW offshore wind turbine generators, 1 HVAC offshore substation platform, associated inter array and export cabling. The generated power will be transmitted to the National Grid via 3 subsea transmission cables making landfall at Carnoustie, Angus, to the Southwest of the development site. Grid connection will

be achieved at the Tealing onshore substation. The second phase of the project will consist of 36 piled foundation structures, with associated 36 Wind Turbine Generators, associated inter array and export cabling and one additional 1 HVAC offshore substation platform. The phase 2 transmission cable is proposed to make landfall at Cockenzie, East Lothian (subject to appropriate licensing).

The Seagreen development site is highlighted below in red, the export cable corridor is highlighted in yellow.

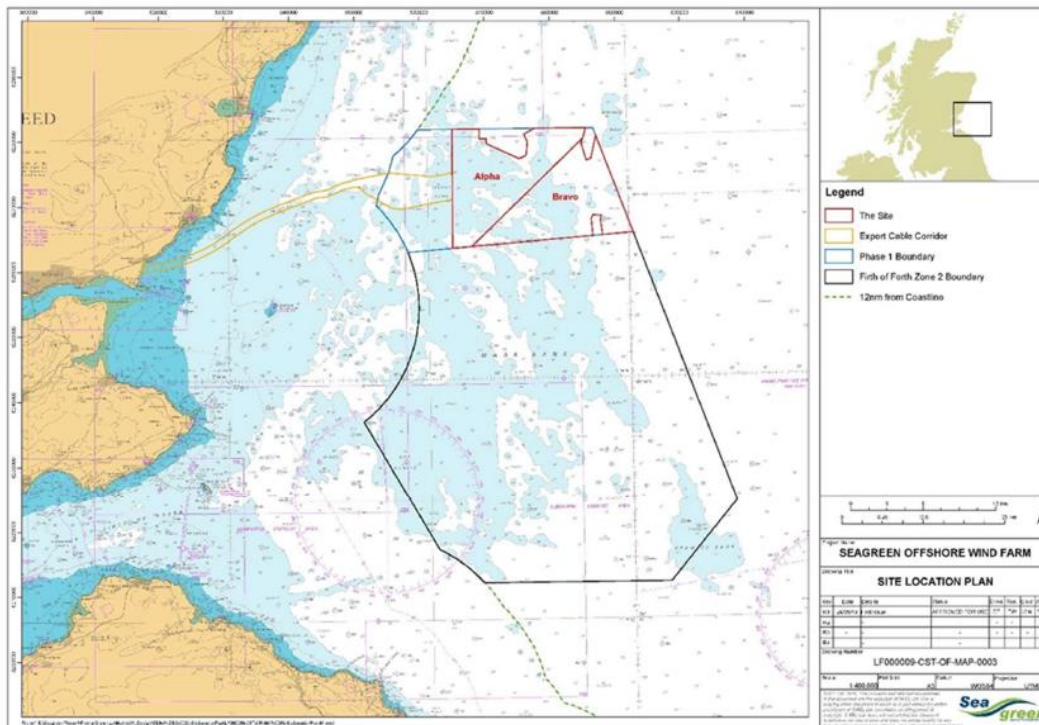


Fig 1 – Seagreen offshore wind farm location and export cable corridor.

1. Contact details for Marine Coordination

The following contact can provide more information if required.

Telephone Number (24/7 Operations)	+44 (0) 333 344 5255
Email for Marine Coordinator	seagreenmarinecoordination@sse.com
Address	Seagreen Wind Energy Ltd, Inchbraoch House Montrose Port Authority, South Quay Ferryden, Montrose, Angus DD10 9SL

2. Ongoing Operations

2.1 Export Cable Landfall works.

Works continue at the export cable landfall site. Installation of three export cable ducts is now complete. Cement bound sand and final backfill operations have been completed. Placement of the top and bottom layers of rock revetment will commence this week with Pile extraction operations scheduled to commence next week. The landfall works area is shown below in Fig 2.



Fig 2 – Landfall works area located at Carnoustie Barry Golf Links.

3. Pre-construction Unexploded Ordnance and Boulder clearance works.

3.1 Unexploded Ordnance & Boulder clearance Geophysical Survey works.

An unexploded ordnance and boulder clearance geophysical survey will take place within the Seagreen Offshore Wind Farm site boundary. The survey vessel, Kommandor Iona will arrive on site this week and utilise towed array equipment with side scan sonar, sub bottom profiler and magnetometer to complete the survey of the remaining WTG locations.

The survey vessel is expected to arrive at site on or around Wednesday the 14th of July. Survey works are expected to be concluded by August 21 however this period may be extended due to weather conditions.

The coordinates of the Seagreen site boundary are below in Table 1 and shown in Fig 1. Details of the survey vessel, Kommandor Iona are shown in Table 2.

ID	Latitude (DDM WGS 84)	Longitude (DDM WGS 84)
01	56° 40.631' N	1° 43.829' W
02	56° 40.606' N	1° 36.151' W
03	56° 39.317' N	1° 36.884' W
04	56° 37.913' N	1° 36.151' W
05	56° 39.923' N	1° 34.627' W
06	56° 31.903' N	1° 29.311' W
07	56° 31.724' N	1° 33.882' W
08	56° 32.983' N	1° 34.195' W
09	56° 33.051' N	1° 35.583' W
10	56° 31.666' N	1° 35.352' W
11	56° 30.803' N	1° 56.378' W
12	56° 40.653' N	1° 56.226' W
13	56° 40.648' N	1° 52.170' W
14	56° 39.836' N	1° 51.101' W
15	56° 38.138' N	1° 46.249' W
16	56° 38.383' N	1° 45.181' W
17	56° 40.157' N	1° 45.487' W

Table 1 – Site Boundary coordinates.

Vessel Name – Kommandor Iona	
General Description and Dimensions:	Survey vessel. 72.5m LOA, 14.9m beam, 6.5m draught
Call Sign:	GAAK
MMSI:	235003070
Satellite communications details	+44 1224 980812
Direct Bridge/ Masters Number	+44 (0) 1224 085571
Onshore Representative:	Alexandru Lepadatu, Alexandru.Lepadatu@subsea7.com +31(0)61 057 48 75
On-board Survey rep.	Gary Howes, +44 (0) 7919 155748
Offshore Fisheries Liaison Officer	Hamish McPherson, +44 (0) 7770 284947.



Table 2 – Survey Vessel Kommandor Iona

3.2 Potential Unexploded Ordnance Identification Survey

A Potential Unexploded Ordnance (pUXO) identification survey will take place within the Seagreen Offshore Wind Farm site boundary. The vessel, Glomar Worker will utilise a ROV mounted magnetometer and video camera to conduct the survey of numerous targets to identify any possible UXO risk. Wind Turbine

Generator positions, Inter Array Cable routes and 1 Offshore Sub-station location within the Seagreen site boundary will be surveyed.

Survey works are expected to be concluded by July 21 however this period may be extended due to weather conditions.

The coordinates of the Seagreen site boundary are above in Table 1 and shown in Fig 1. Details of the survey vessel, Glomar Worker are shown below in Table 3.

Vessel Name – Glomar Worker	
General Description and Dimensions:	Survey vessel. 60.0m LOA, 15.6m beam, 4.5m draught
Call Sign:	3EKK8
MMSI:	352110000
Satellite communications details	+87 0773281351 & +31 852088024
Direct Bridge/ Masters Number	+31 645027717
Onshore Representative:	Alexandru Lepadatu, Alexandru.Lepadatu@subsea7.com +31(0)61 057 48 75
Onboard Survey rep.	Alice Bamkin +44 (0)7845 554353



Table 3 – Survey Vessel Glomar Worker.

4. Distribution List

A central list of recipients is maintained by Seagreen Marine Coordination, if you are not the appropriate recipient or do not wish to receive these notices please contact Marine Coordination as per the details in section 1 of this notice.

5. Website

The official website for Seagreen Offshore Wind Farm can be found at

<https://seagreenwindenergy.com>

This contains all Seagreen Weekly Notices of Operations and Notices to Mariners, together with a large amount of general information about the project.

There is also a Twitter feed at [@seagreenwind](https://twitter.com/seagreenwind)

This document contains proprietary information belonging to Seagreen Wind Energy Ltd or affiliated companies and shall be used only for the purpose for which it was supplied. It shall not be copied, reproduced, disclosed or otherwise used, nor shall such information be furnished in whole or in part to third parties, except in accordance with the terms of any agreement under which it was supplied or with the prior consent of Seagreen Wind Energy Ltd and shall be returned upon request. © Copyright of Seagreen Wind Energy Ltd



Document Reference

LF000009-MIP-MA-MAN-NOT-0001

Rev: 31

Page 8 of 8
